


PLAN IMPLEMENTARE



Documenta
powered by ORACLE Database

 **INFRA**SOFT
Infrastructure Business


ORACLE PARTNER

- Document Management System -


www.infrasoft.ro

Planul de proiect

	i	Task Name	Duration	Start	Finish	Prede
1		+ Kick-off	5 days	Mon 5/17/10	Fri 5/21/10	
4		+ Analiza	10 days	Mon 5/24/10	Fri 6/4/10	1
7		+ Configurare si particularizare	15 days	Mon 6/7/10	Fri 6/25/10	4
10		+ Instalare	3 days	Mon 6/28/10	Wed 6/30/10	7
14		+ Validare	13 days	Thu 7/1/10	Mon 7/19/10	10
17		+ Migrare date	7 days	Tue 7/20/10	Wed 7/28/10	14
20		+ Training	5 days	Thu 7/29/10	Wed 8/4/10	17
24		Acceptanta functionala(AF)	0 days	Wed 8/4/10	Wed 8/4/10	20
25		Go live	1 day	Thu 8/5/10	Thu 8/5/10	24
26		Asistenta	5 days	Fri 8/6/10	Thu 8/12/10	25
27		Suport si mentenanta	5 days	Fri 8/13/10	Thu 8/19/10	26

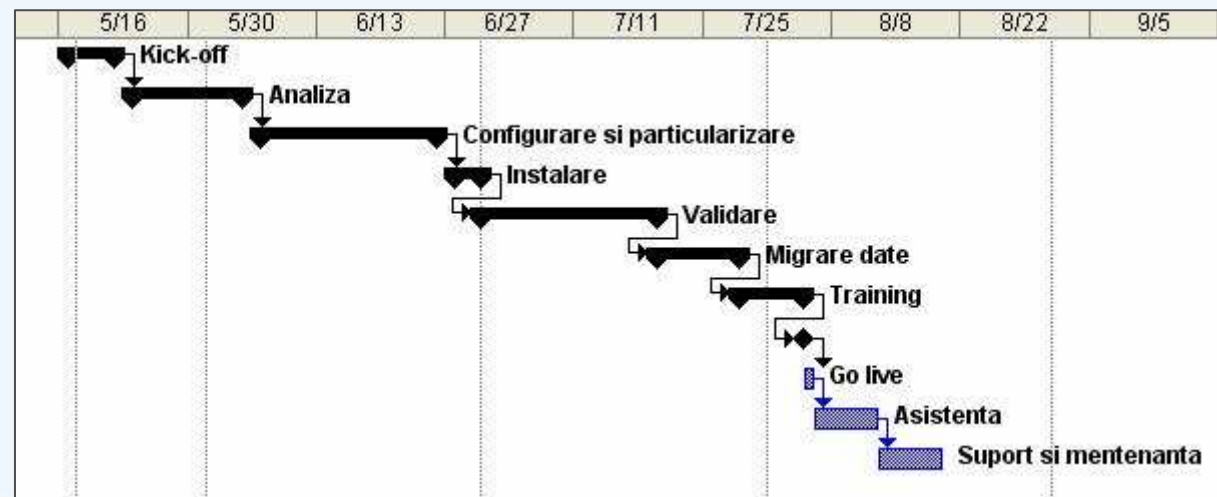

Kick-off

		Task Name	Duration	Start	Finish	Prede
1		<input type="checkbox"/> Kick-off	5 days	Mon 5/17/10	Fri 5/21/10	
2		Stabilire echipa de proiect	2 days	Mon 5/17/10	Tue 5/18/10	
3		Aprobare plan de proiect	5 days	Mon 5/17/10	Fri 5/21/10	

- ❖ **Stabilirea obiectivelor**
- ❖ **Stabilirea echipei de proiect**
- ❖ **Elaborarea si aprobarea planului de proiect**
- ❖ **Metodologie (bazata pe ORACLE CDM)**
- ❖ **Strategia de validare si trecere in exploatare**



Analiza

4	Analiza	10 days	Mon 5/24/10	Fri 6/4/10	1
5	Definirea cerintelor	10 days	Mon 5/24/10	Fri 6/4/10	
6	Analiza sistemului existent	5 days	Mon 5/24/10	Fri 5/28/10	

- ❖ **Analiza sistemului existent**
- ❖ **Definirea detaliata a cerintelor**
- ❖ **Analiza interfetelor sistemului**
- ❖ **Elaborarea si aprobarea Business Requirements Definition Document**
- ❖ **Utilizarea minutelor de sedinta**
- ❖ **Compliance matrix**



Configurare si instalare

7	<input type="checkbox"/> Configurare si particularizare	15 days	Mon 6/7/10	Fri 6/25/10	4
8	Configurare	10 days	Mon 6/7/10	Fri 6/18/10	
9	Particularizare	5 days	Mon 6/21/10	Fri 6/25/10	8
10	<input type="checkbox"/> Instalare	3 days	Mon 6/28/10	Wed 6/30/10	7
11	Pregatire server	1 day	Mon 6/28/10	Mon 6/28/10	
12	Instalare Oracle	1 day	Tue 6/29/10	Tue 6/29/10	11
13	Instalare Documenta	1 day	Wed 6/30/10	Wed 6/30/10	12

- ❖ **Configurare**
- ❖ **Implementarea cerintelor specifice**
- ❖ **Pregatirea serverului**
- ❖ **Instalare ORACLE**
- ❖ **Instalare Documenta**
- ❖ **Distribuirea aplicatiei la utilizatori**



Validarea sistemului

14	<input type="checkbox"/> Validare	13 days	Thu 7/1/10	Mon 7/19/10	10
15	Aprobare scenarii de test	3 days	Thu 7/1/10	Mon 7/5/10	
16	Validare	10 days	Tue 7/6/10	Mon 7/19/10	15

- ❖ **Elaborarea planului de testare**
- ❖ **Elaborarea scenariilor de testare (functionale, integrare, compatibilitate, performanta, negative)**
- ❖ **Aprobarea scenariilor**
- ❖ **Stabilirea echipei de testare**
- ❖ **Parcurgerea scenariilor**
- ❖ **Rezolvarea problemelor identificate**



Migrarea datelor

17	<input type="checkbox"/> Migrare date	7 days	Tue 7/20/10	Wed 7/28/10	14
18	Identificare surse date	2 days	Tue 7/20/10	Wed 7/21/10	
19	Migrare	5 days	Thu 7/22/10	Wed 7/28/10	18

- ❖ **Identificarea surselor de date**
- ❖ **Transpunerea surselor de date pe formatul standard de import**
- ❖ **Validari si corectii de date**
- ❖ **Importul datelor in sistem**
- ❖ **Validarea datelor in sistem (chei de control)**



Training

20	<input type="checkbox"/> Training	5 days	Thu 7/29/10	Wed 8/4/10	17
21	Livrarea manualelor	1 day	Thu 7/29/10	Thu 7/29/10	
22	Instruire administratori	2 days	Fri 7/30/10	Mon 8/2/10	21
23	Instruire utilizatori	2 days	Tue 8/3/10	Wed 8/4/10	22

- ❖ **Livrarea manualelor (electronic & hard copy)**
- ❖ **Training administrator**
- ❖ **Training utilizatori**
- ❖ **Workshop**



Go Live

24	Acceptanta functionala(AF)	0 days	Wed 8/4/10	Wed 8/4/10	20
25	Go live	1 day	Thu 8/5/10	Thu 8/5/10	24
26	Asistenta	5 days	Fri 8/6/10	Thu 8/12/10	25
27	Suport si mentenanta	5 days	Fri 8/13/10	Thu 8/19/10	26

- ❖ **Acceptanta functionala**
- ❖ **Stabilirea strategiei de trecere in exploatare curenta (pilot, operare paralela, direct)**
- ❖ **Trecerea in operare curenta**
- ❖ **Asistenta post-productie**
- ❖ **Suport si mentenanta**





 **INFRASOFT**
Infrastructure Business

www.infrasoft.ro
